ID	Task Name	Duration	Start	Finish	Predece
1					
2	**KING ROAD EAST AND WEST**	**11 days**	**Tue 8/18/09**	**Tue 9/1/09**	
3	PLACE BMP'S	1 day	Tue 8/18/09	Tue 8/18/09	
4	POTHOLE SEWER LINE	1 day	Wed 8/19/09	Wed 8/19/09	3
5	GRIND AND PLACE AB PARTIAL	2 days	Wed 8/19/09	Thu 8/20/09	4SS
6	TRIM AB AND PAVE PARTIAL	1 day	Fri 8/21/09	Fri 8/21/09	5
7	TRENCH AND CAP SEWER LINE KING	1 day	Mon 8/24/09	Mon 8/24/09	6
8	GRIND AND PLACE AB REMAINING	1 day	Mon 8/31/09	Mon 8/31/09	7
9	TRIM AB AND PAVE REMAINING	1 day	Tue 9/1/09	Tue 9/1/09	8
10					
11	**BIKE PATH**	**4 days?**	**Mon 8/24/09**	**Thu 8/27/09**	
12	PLACE BMP'S BIKE PATH	1 day?	Mon 8/24/09	Mon 8/24/09	3
13	EXCAVATE BIKE PATH	2 days	Mon 8/24/09	Tue 8/25/09	6
14	PLACE AB BIKE PATH	2 days	Tue 8/25/09	Wed 8/26/09	13FS-1
15	FINISH AB BIKE PATH AND PAVE	1 day	Thu 8/27/09	Thu 8/27/09	14
16					
17	**BRACE ROAD**	**3 days**	**Mon 9/7/09**	**Wed 9/9/09**	
18	GRIND AND PLACE AB	2 days	Mon 9/7/09	Tue 9/8/09	9
19	TRIM AB AND PAVE	1 day	Wed 9/9/09	Wed 9/9/09	18

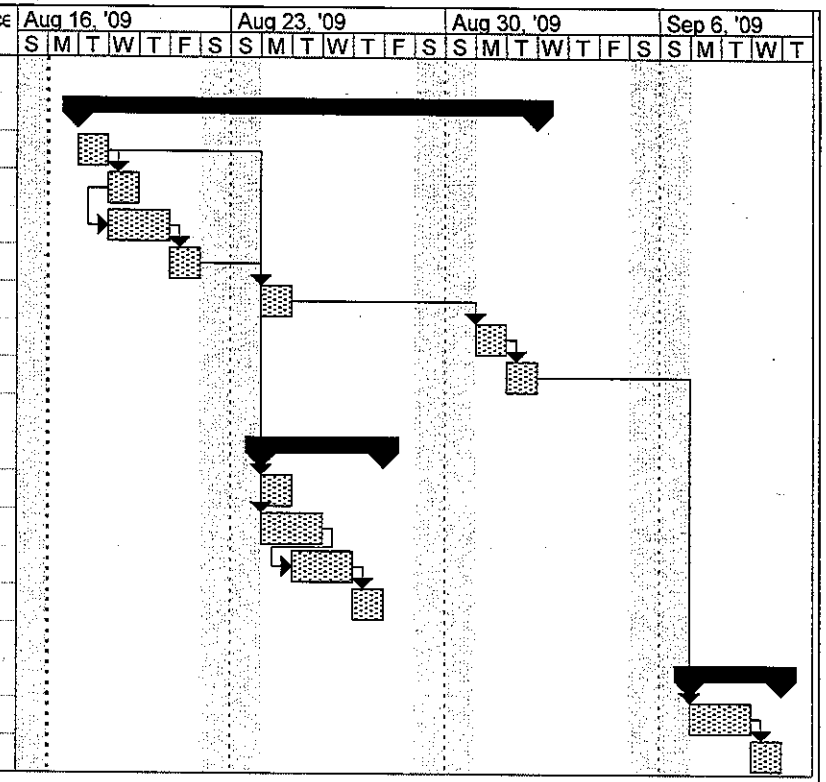

Project: Base Line
Date: Mon 8/17/09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
